

Harrison Elem. Weekly Blitz: May 1st, 2020



Harrison Elementary: The stage bearing walls have been completed and the masons have moved to the gym, kitchen, and mechanical walls in Area A. In Area B, Steel is being set in sequence #2 while the metal decking gets installed in sequence #1. Electrical and plumbing rough-ins are being installed in bearing block.



Crosby Elem. Weekly Blitz: May 1st, 2020



Crosby Elementary: Bearing walls in Area A begin to rise with the start of the gym. The stage and cafeteria walls have been laid out this week. In Area B, steel in sequence #1 is being set with metal decking closely behind. Electrical and plumbing rough-ins are being installed in bearing block.



Miami Whitewater Weekly Blitz: May 1st, 2020



Miami Whitewater Campus: Bearing walls in Area B continue to rise in preparation for steel sequences #1 and #2. The site has been prepped for the delivery of steel and the crane. Electrical and plumbing rough-ins continue in Area B. The installation of the gas main across the MWW Elem and the Junior High site continues.





Junior High Weekly Blitz: May 1st, 2020



Harrison Junior High: The concrete footers in Area C will be complete this week followed by the foundation block in Area B . Underground electric and plumbing is being installed across all 3 areas. In Area A, the East half of the slab on grade was poured last week and the West half will be poured this week.



Elementary School Floor Plans

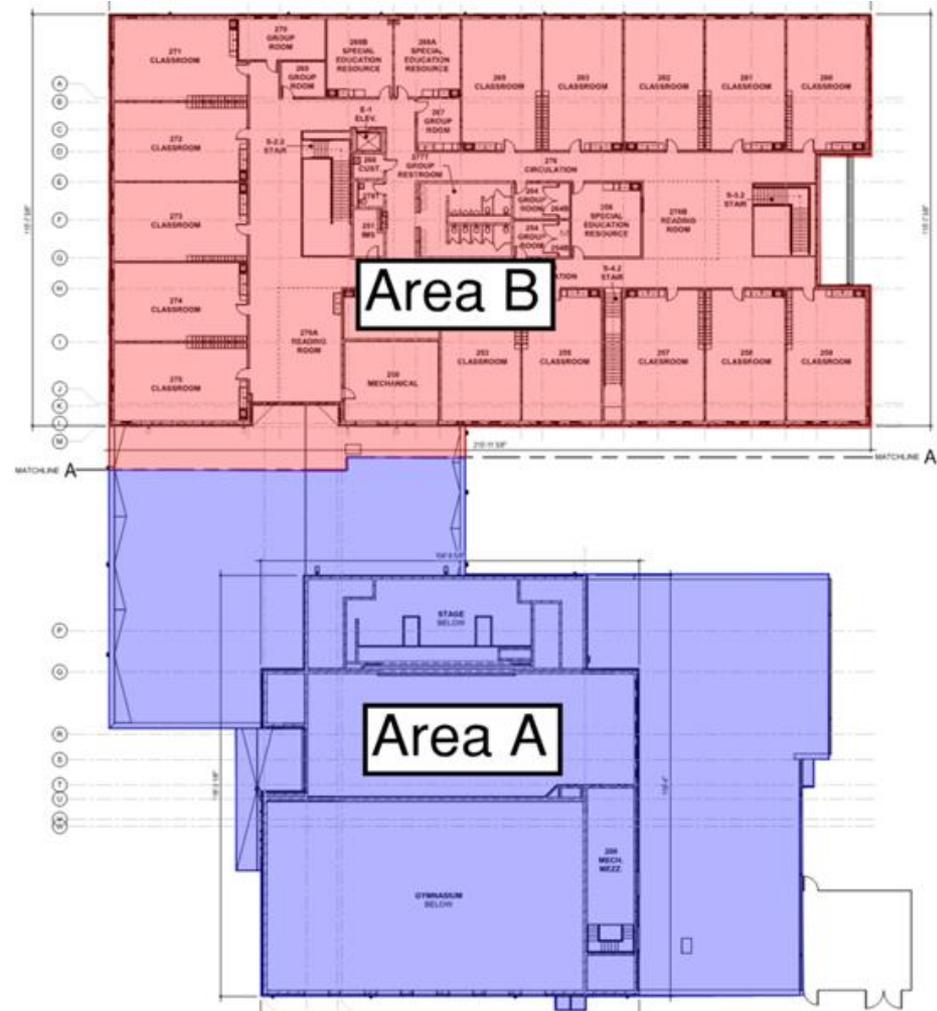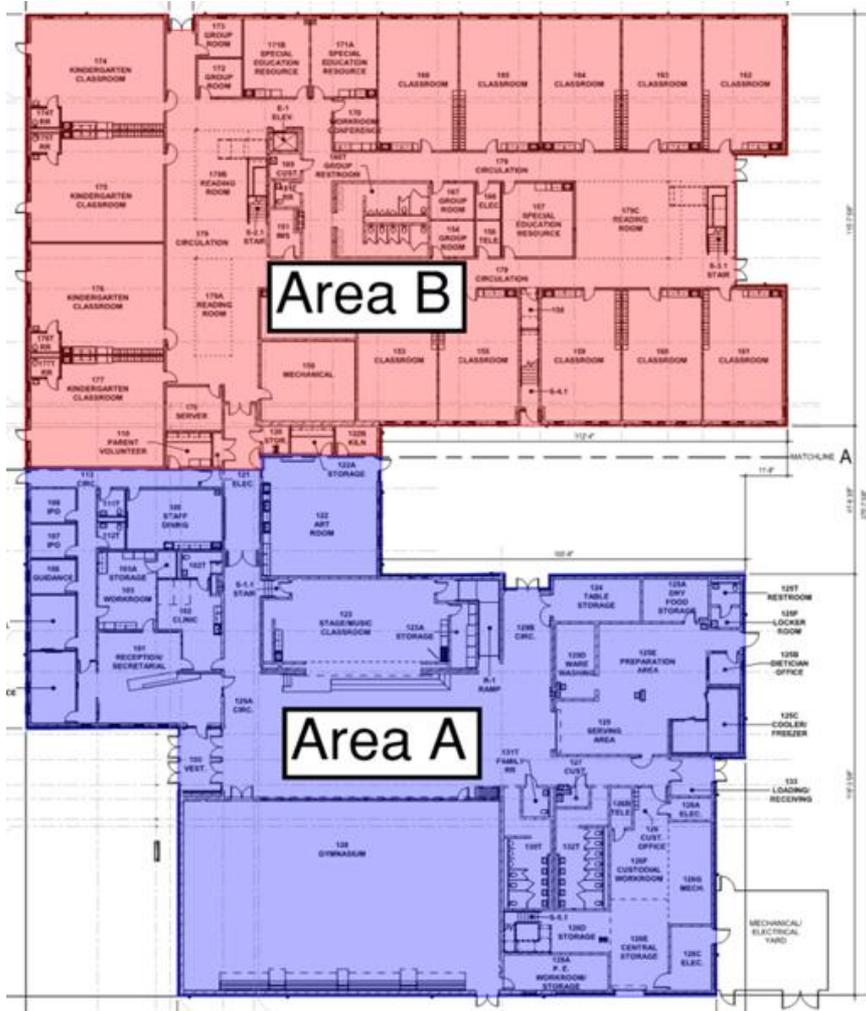

Junior High School Floor Plans

