

# Harrison Elem. Weekly Blitz: May 22<sup>nd</sup>, 2020



**Harrison Elementary:** The gym, mechanical, and kitchen bearing walls continue to rise in Area A. In Area B, half of the 2<sup>nd</sup> floor concrete slab will be poured this week. The 1<sup>st</sup> floor interior walls are being laid out to start framing next week. In-wall and above ceiling rough-in for MEP piping and duct continues in both Areas A and Area B.



# Crosby Elem. Weekly Blitz: May 22<sup>nd</sup>, 2020



**Crosby Elementary:** The interior gym bearing walls and the cafeteria walls continue to rise in Area A. In the South half of Area B, steel has been set for the 2<sup>nd</sup> floor and metal decking is being installed. Electrical and plumbing rough-ins are being installed in bearing block.



# Miami Whitewater Weekly Blitz: May 22<sup>nd</sup>, 2020



**Miami Whitewater Campus:** 1<sup>st</sup> floor bearing walls in Area B are nearing completion in preparation for 2<sup>nd</sup> floor steel. Steel columns and beams in the South half of Area B have been set and metal decking is being installed. Electrical and plumbing rough-ins are being installed in bearing block.





# Junior High Weekly Blitz: May 22<sup>nd</sup>, 2020



**Harrison Junior High:** Foundation block continues in Area C while bearing walls continue to rise in Area A. The concrete slab in the West half of Area B will be poured this week. MEP underground in Area C is near completion and MEP rough-ins are being installed in bearing block in Area A.



# Elementary School Floor Plans

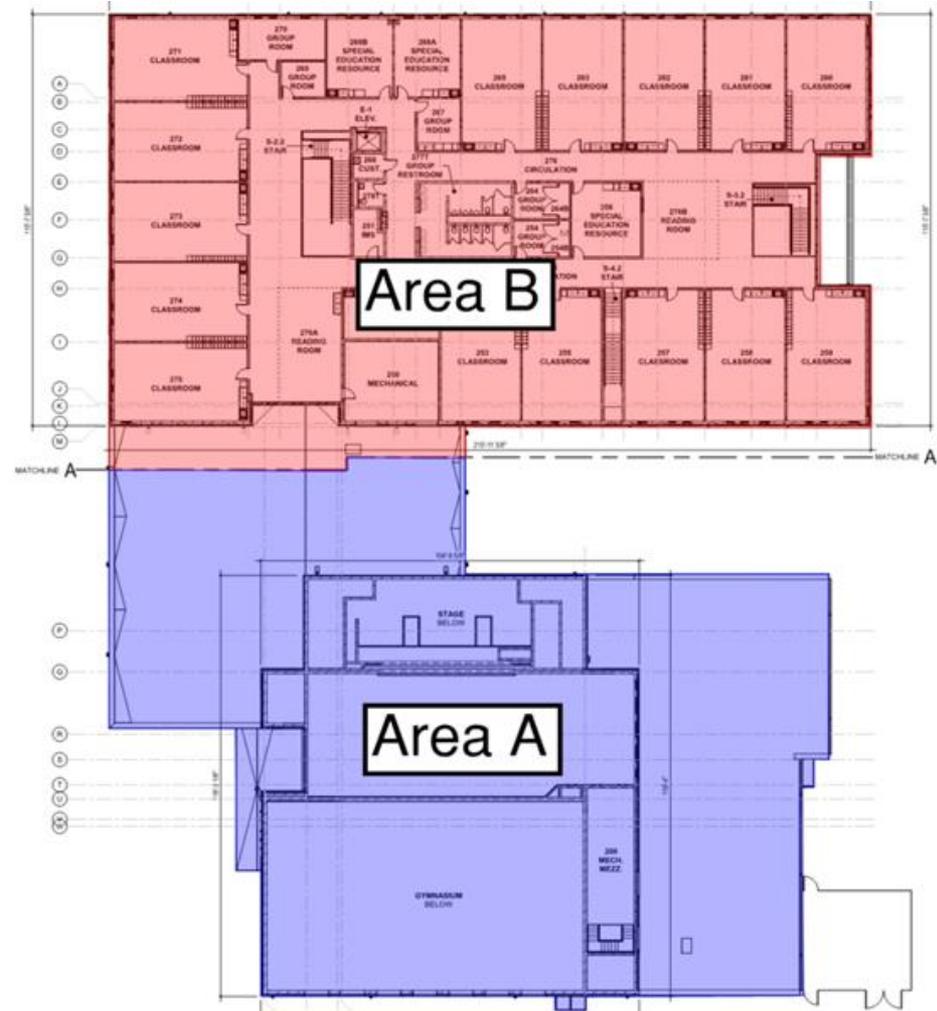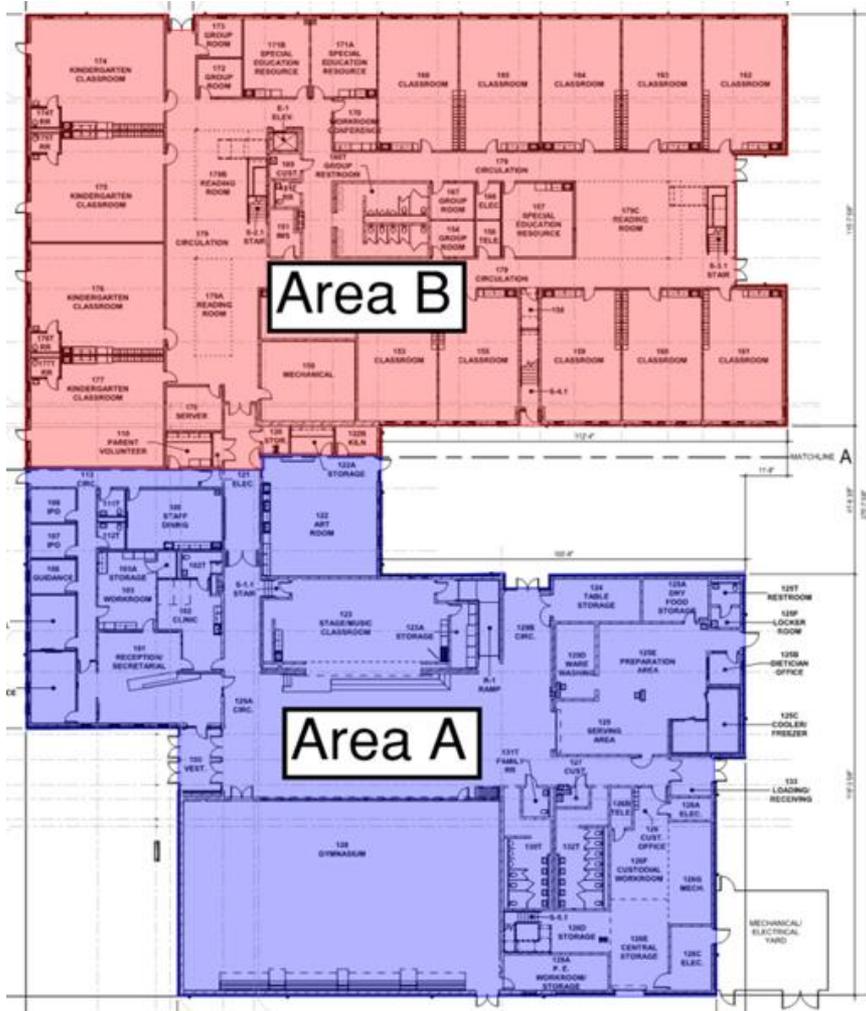

# Junior High School Floor Plans

