


Harrison Elem. Weekly Blitz: July 10th, 2020




Harrison Elementary: The Area A kitchen and mechanical block walls have been completed and the admin walls are rising. In Area B, the roof installation continues and the metal stairs are being set in stairwells. The 2nd floor interior walls and door frames are being framed and set. In-wall and above ceiling MEP rough-in continues in both Areas.

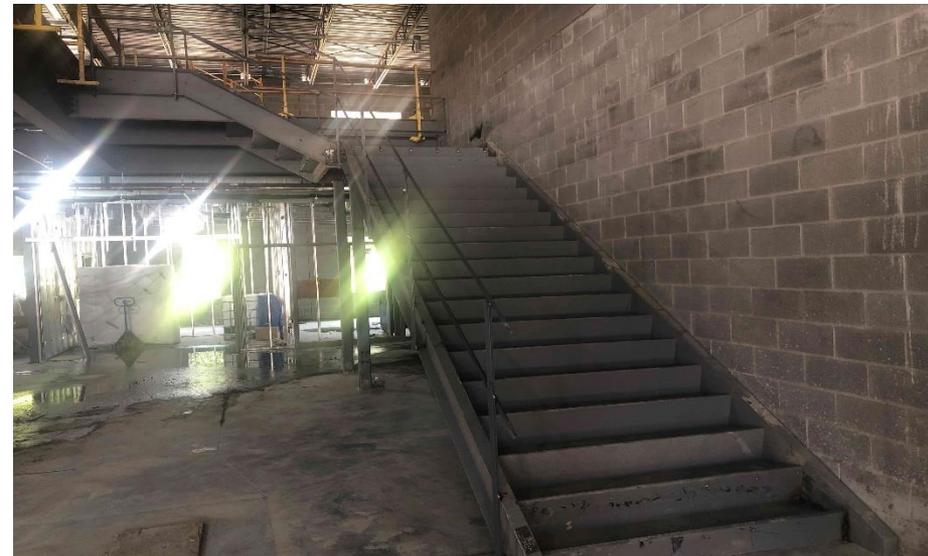

Crosby Elem. Weekly Blitz: July 10th, 2020



Crosby Elementary: In Area A, the metal roof decking is being installed in the gym, cafeteria, and stage. In Area B, the 2nd floor block walls are rising to the roof level and the 1st floor interior walls and door frames have been framed and set. In-wall and above ceiling MEP rough-in continues in both Areas.

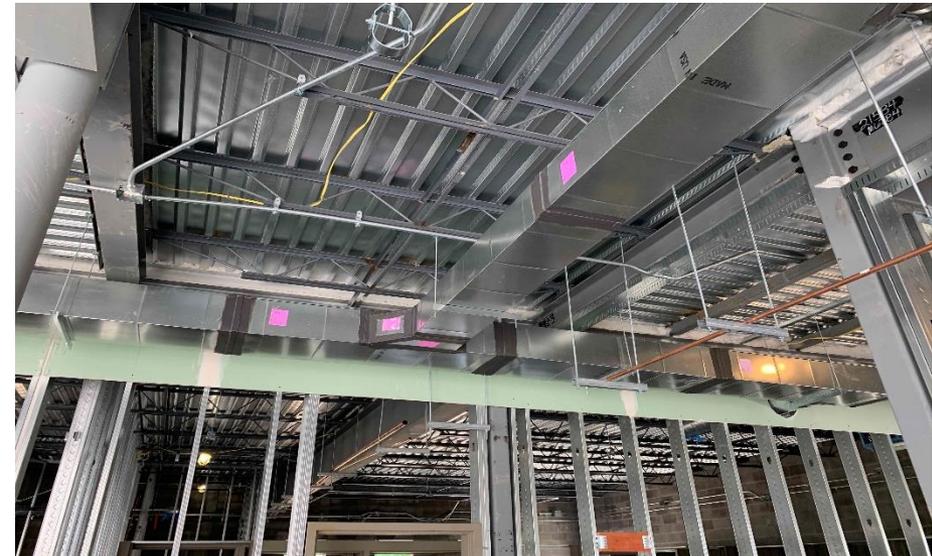

Miami Whitewater Weekly Blitz: July 10th, 2020



Miami Whitewater Elementary: The gym and stage bearing walls continue to rise and the roof steel has been set at the gym in Area A. In Area B, the 1st floor interior walls have been framed in and the door frames are being set. The elevated concrete slab in the North half of the 2nd floor and the air handling unit concrete pads have been poured. In-wall and above ceiling MEP rough-in continues.





Junior High Weekly Blitz: July 10th, 2020



Harrison Junior High: The 2nd floor of the academic wing has been prepped for next week's elevated concrete pours. Bearing block walls continue to rise in the kitchen and gym in Areas B & C. Metal stairs are being installed in Area A and structural steel is being set in the East half of Area B. In-wall and above ceiling MEP rough-in continues.



Elementary School Floor Plans

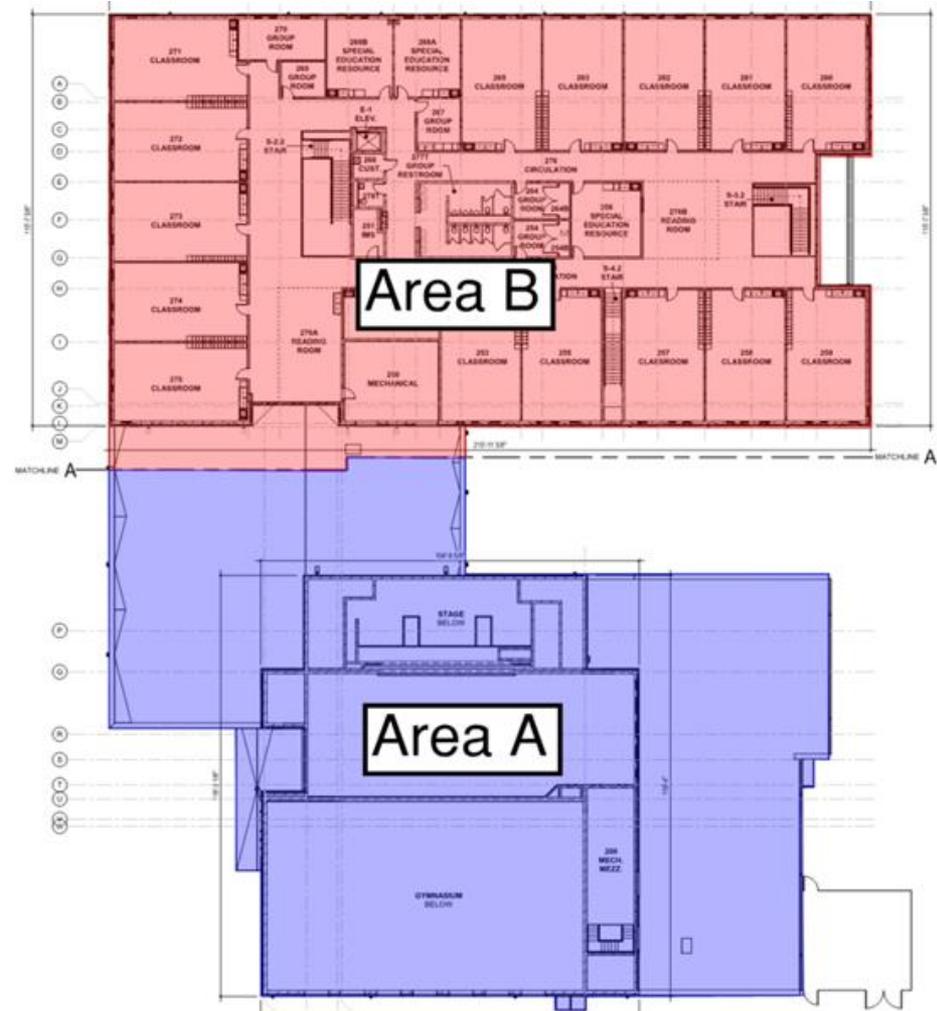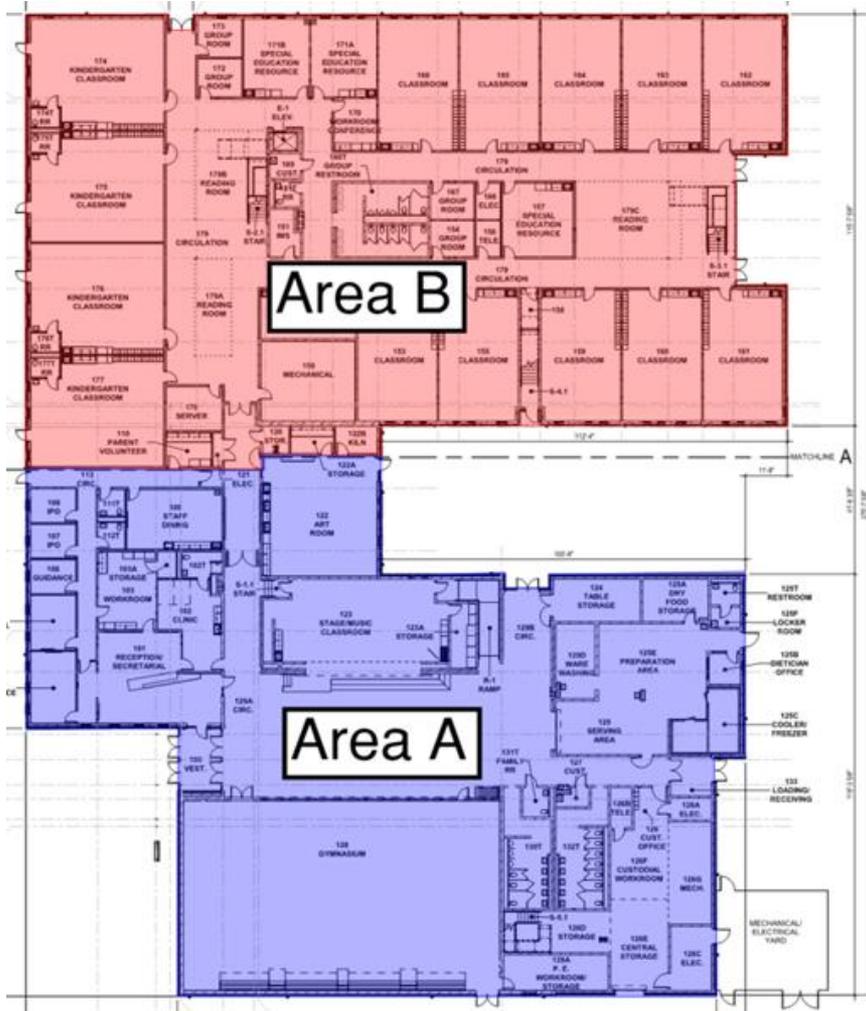

Junior High School Floor Plans

