



# Harrison Elem. Weekly Blitz: January 15<sup>th</sup>, 2021

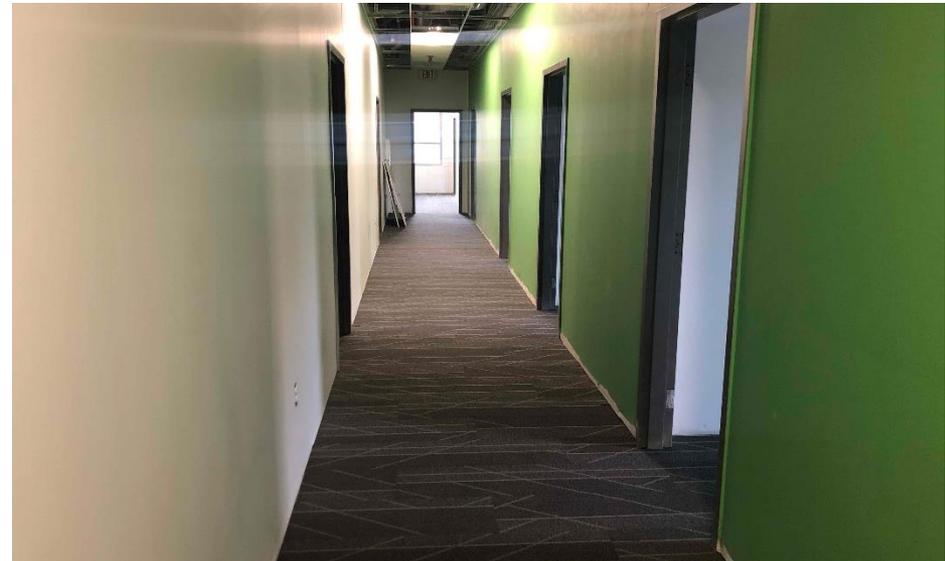

**Harrison Elementary:** Final painting and soft flooring installation continues throughout the academic and administration wing. Ceiling pads have been dropped in place in Area A. Miscellaneous items are being installed throughout the building such as toilets, sinks, wall protection, doors, marker boards, and kitchen equipment.

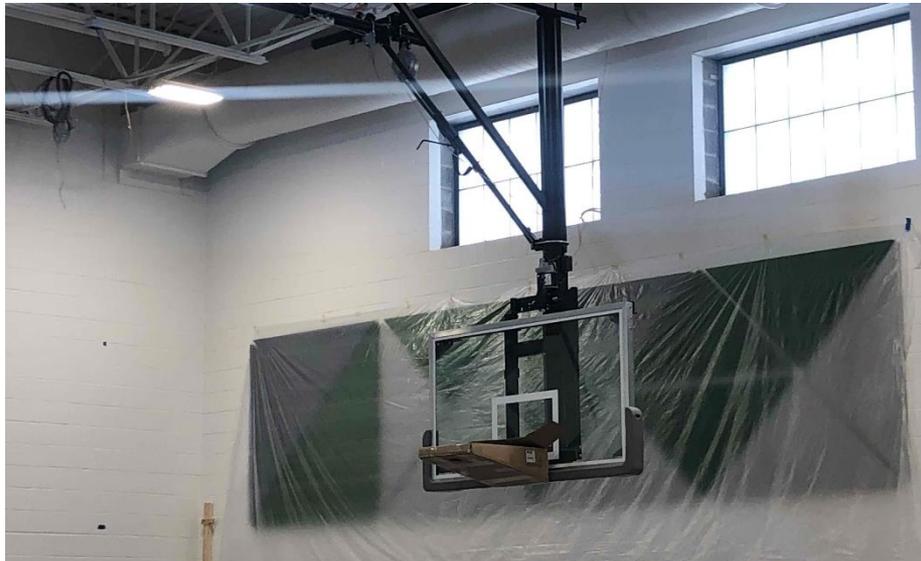

# Crosby Elem. Weekly Blitz: January 15<sup>th</sup>, 2021



**Crosby Elementary:** In Area A, painting continues in the gym and cafeteria while permanent lights are being installed in the art room. Interior window trim pieces and ceiling tiles are being installed in Area B. Resinous and soft flooring has begun in the Area B restrooms and classrooms. Metal gutters are being installed on the exterior of the building and concrete sidewalk work continues.



# Miami Whitewater Weekly Blitz: January 15<sup>th</sup>, 2021



**Miami Whitewater Elementary:** In Area A, lights are being installed in the administration wing while painting continues in the gym, student dining and at the stage. Ceiling pads are being dropped in Area B and cabinet installation continues throughout the building. Brick and metal gutter work continues along the exterior of Area B walls.





# Junior High Weekly Blitz: January 15<sup>th</sup>, 2021



**Harrison Junior High:** Roof installation continues above the administration area while the fireproofing underneath is nearly completed. Brick continues along the North wall of Area A. Drywall is being hung on the 2<sup>nd</sup> floor of Area B and being finished on the 3<sup>rd</sup> floor of Area A. Painting, lighting, and ceiling grid installation continues on the 1<sup>st</sup> and 2<sup>nd</sup> floors of Area A.



# Elementary School Floor Plans

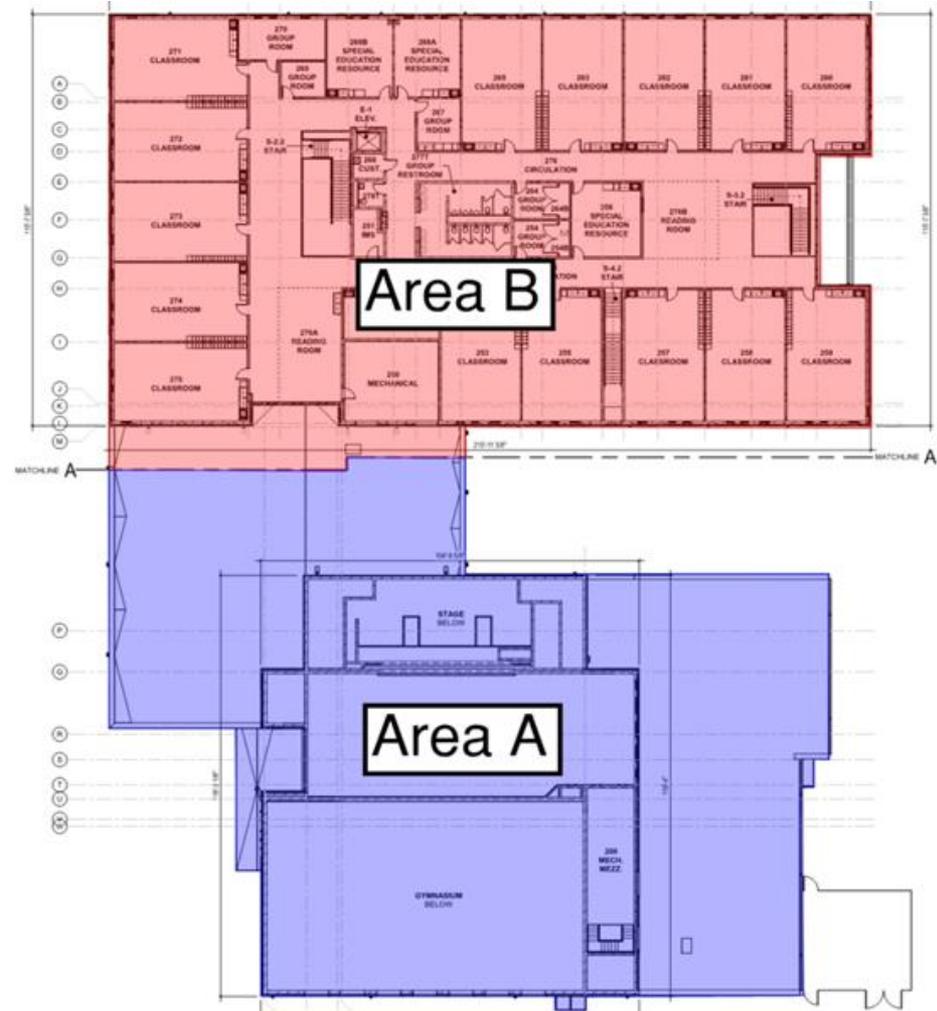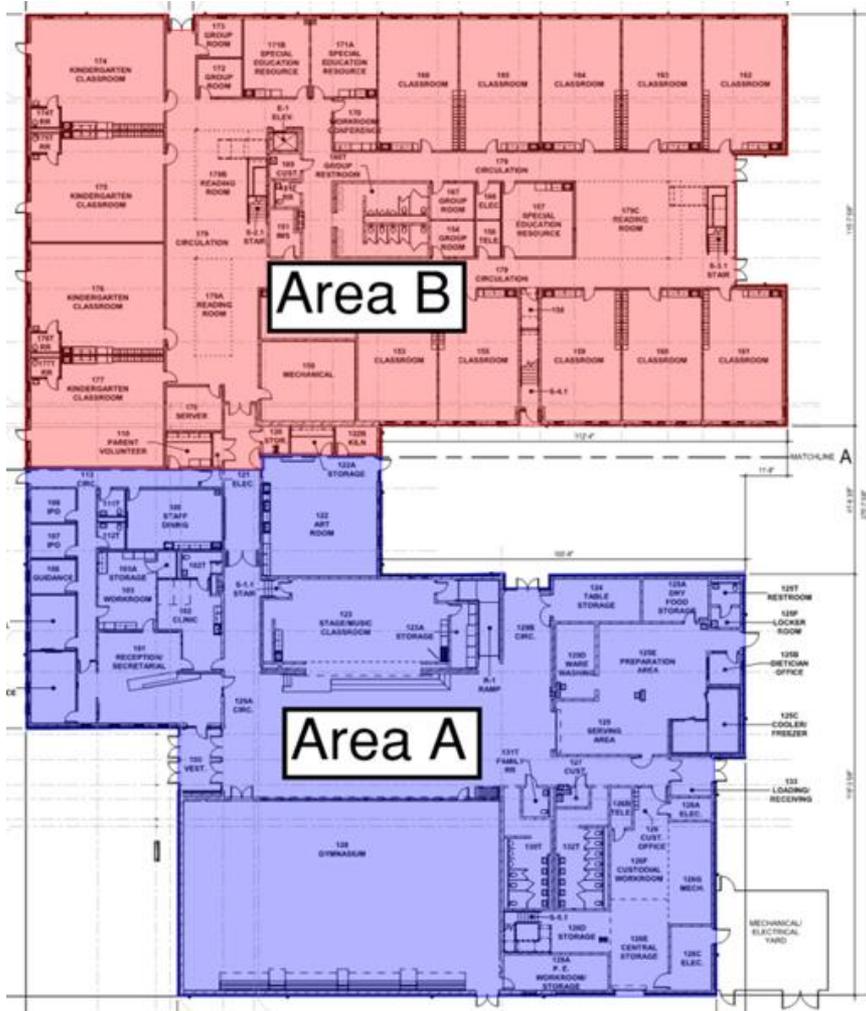

# Junior High School Floor Plans

